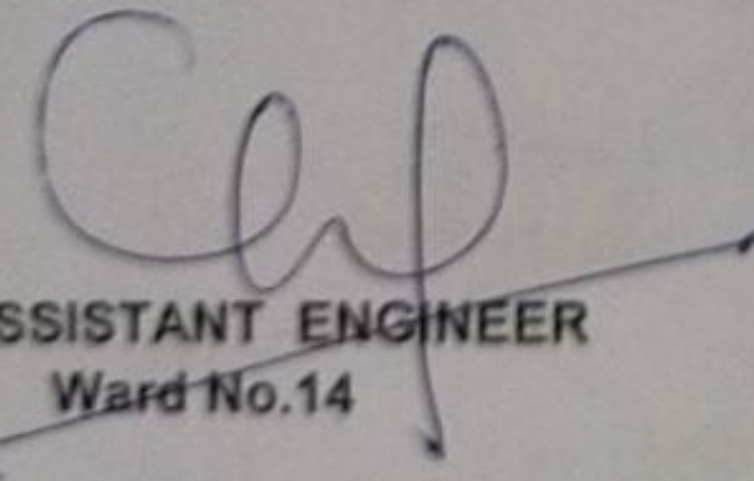




Completion Report

Name of Work	REPAIRS & MAINTENANCE OF BOREWELLS AT SIDEDAHALLI VILLAGE LIMIT IN WARD NO 14 BAGALAGUNTE		
Sanctioned Estimate No.& Date	EE/DD/AS/ 112/19-20, Dt.17.05.2019		
	EE/DD/TS/ 107/18-19, Dt.02.02.2019		
Head of Account which is Chargeable	P-1771		
Instrument Order No. & Date	EE/DD/WO/ 480 /19-20, Dt.02.01.2020		
Name of Contractor	Muniraj Naik		
Time Stipulated for Completion of work	90 days		
Delay in execution of work	Nil		
Measurement recorded in MB	MB No.352/08-09		
Page No	35176-35178		
check Measurement of the Asst			
Exe. Eng./ Exe.Eng. On			
Name of the Office / Official	Asst.Executive Engineer T.Dasarahalli Sub Division		
incharge of the work			
a)Assistant Engineer	Chetank K M		
b) Asst. Exe. Engineer	M B Jayakumar		
Sanctioned Estimate amount	Amount claims as per actually vide as per bills	Excess	Savings (Rs)
30.00 Lakhs	2760399.00	—	239601.00

- 1) Certified that the above work has been Completed within the stipulated time nited in the
- 2) Certified that the Contractor has delayed and completed the work for which necessary fine recovered
- 3) Certified that the above work has been executed by the contractor satisfactory in


ASSISTANT ENGINEER
Ward No.14


ASSISTANT EXECUTIVE ENGINEER
T.DASARAHALLI SUB-DIVISION
BANGLORE


EXECUTIVE ENGINEER
Bruhat Bangalore Mahanagara Palike,
Dasarahalli Division, Bangalore-57
